HALF-CENT SALES TAX PROJECTS

MONTHLY REPORT NOVEMBER **2024**



THANK YOU VOTERS!





BETTER **ROADS**,
MORE **SIDEWALKS**,
AND **CLEANER RIVERS**.

HIGHLIGHTS



PROJECTS

California Blvd Widening: A public information meeting was held on September 14, 2022. The consultant then incorporated the comments received and presented a concept to the City Council on March 20, 2023. A draft of the concept typical section, including an access management plan, was included in the presentation. City Council subsequently adopted the typical section and the access management plan. An additional public meeting was held on January 25th, 2024. The project is ready to move into the design phase, currently anticipated FY 25/26. Staff attended three HOA meetings for Lake Charles to help answer questions about the project.

Sidewalks: Construction on Import Drive (Phase 2) from Inca Terrace to Savage Boulevard was completed in December 2023. Final acceptance of the project is pending. Construction on Abingdon Avenue from Import Dr. to Savona Blvd. began in December 2023 and is completed, pending final acceptance. Lakehurst Sidewalk Ph. II is in design. More information regarding the sidewalk master plan including planned sidewalks can be found at www.cityofpsl.com/sidewalks.

Repaving: Sixteen and four-tenths (16.4) miles were proposed to be repaved in FY 23/24 utilizing \$2,600,000 in Sales Tax funding. So far, 14.80 miles have been repaved in the Sandpiper Bay, Riverview, Oak Hammock, and Floresta Gardens Neighborhoods this fiscal year. The remaining 1.6 miles were delayed due to weather and will be repaved by early 2025. More information regarding the repaving master plan and streets to be repaved can be found at www.cityofpsl.com/repaving.

Floresta Drive Phase II Improvements: Construction along Floresta Drive Phase II continues. The contractor has been working to complete curb, irrigation, stamped concrete and median activities. The contractor started installing landscaping and is placing final friction course for the roadway. For more information on all phases of the Floresta Drive Project, please visit www.florestadrive.com.

US 1 Improvements: The US 1 Landscaping project is complete and provides beautification improvements including irrigation and landscaping from the Martin County line to 150 feet North of SE Huffman Road. The project included large and small plants and turf as well as irrigation in some areas and stamped color concrete.





\$1,032,035.30

10-YEAR GOAL

\$18,300,000.00

LOCATIONS	PERCENTAGE COMPLETE	START DATE	END DATE	ESTIMATED BUDGET	REVISED BUDGET ¹	CONTRACT VALUE
Cashmere IntersectionDesignCEI*Construction	100%	02/2019 2/4/19 10/2019 10/2019	03/2020 5/31/19 03/2020 03/2020	\$500,000 \$55,000 \$75,000 \$370,000	N/A	\$54.353 \$1,471 \$223,579
Bayshore Intersection Design CEI* Construction	100%	02/2019 2/4/19 10/2019 10/2019	03/2020 5/31/19 03/2020 03/2020	\$400,000 \$44,000 \$60,000 \$296,000	N/A	\$43,847 \$34,826 \$386,403
Peacock Intersection	100%	02/2019 2/4/19 10/2019 10/2019	03/2020 5/31/19 01/2020 01/2020	\$300,000 \$33,000 \$45,000 \$222,000	N/A	\$32,900 \$23,70 \$1,7,984
California Intersection Design CEI* Construction		07/2024 07/2024 07/2026 07/2026	12/2027 12/2025 12/2027 12/2027	\$2,000,000 \$220,000 \$300,000 \$1,480,000	\$2,000,000	
California Widening Design ² CEI* Construction	1%	07/2024 07/2024 07/2026 07/2026	12/2027 12/2025 12/2027 12/2027	\$10,000,000 \$1,100,000 \$1,500,000 \$7,400,000	\$15,100,000 \$1,500,000 \$2,000,000 \$11,600,000	\$24,476

^{*}CEI: Construction Engineering Inspection Services



¹ Budgets have been revised for certain projects based upon escalating construction costs, which has been offset by higher-than-expected revenue.

² Pursuant to City Council direction, Staff have expedited the public involvement portion of the conceptual design and access management planning.

SIDEWALKS



\$5,336,390.57

10-YEAR GOAL

\$11,000,000.00

LOCATIONS	PERCENTAGE COMPLETE	START DATE	END DATE	ESTIMATED BUDGET	REVISED BUDGET	CONTRACT VALUE
Import Drive - Phase 2 (Inca to Savage) • Construction	99%	3/2023	12/2023	\$850,000		\$1,285,247
Abingdon Drive (Import to Savona) Construction	99%	12/2023	6/2024	\$650,000		\$621,431
Lakehurst Drive (Bayshore to Ivanhoe) Design		6/2023	4/2024	-	-	





Abingdon Sidewalk



REPAVING



DOLLARS SPENT TOWARDS GOAL \$8,198,547.10 **10-YEAR GOAL**

\$27,500,000.00

LOCATIONS	PERCENTAGE COMPLETE	START DATE	END DATE	ESTIMATED BUDGET	REVISED BUDGET	CONTRACT VALUE
Sandpiper Bay South	100%	10/2023	12/2023	\$524,144	\$533,962	\$534,085
Sandpiper Bay Mid	100%	10/2023	12/2023	\$267,783	\$274,055	\$260,017
Rosser Reserve West		10/2023	9/2024	\$282,903		
Rosser Reserve East		10/2023	9/2024	\$223,998		
Riverview South	100%	10/2023	9/2024	\$314,605	\$302,915	\$299,498
Oak Hammock	100%	10/2023	9/2024	\$401,064	\$401,064	\$396,189
Floresta Gardens Mid	100%	10/2023	9/2024	562,928		\$533,229
Gatlin (PSL Blvd. to I-95)		04/2027	9/2027	\$1,250,000		





Floresta Gardens



TRAFFIC SIGNAL COORDINATION



DOLLARS SPENT TOWARDS GOAL

\$0

10-YEAR GOAL

\$0

LOCATIONS	PERCENTAGE COMPLETE	START DATE	END DATE	ESTIMATED BUDGET	REVISED BUDGET	CONTRACT VALUE
Port St Lucie Boulevard**		10/2027	03/2028	\$900,000		
Crosstown Parkway*		01/2028	06/2028	\$800,000		

^{*}Crosstown Parkway traffic signal adaptive coordination has been removed from the $\frac{1}{2}$ Cent Sales Tax Projects list. This item was expedited and funded by the Crosstown Parkway Extension project. The adaptive coordination went live in May 2020.



^{**}The cost of Port St. Lucie Boulevard Adaptive Coordination was included in a bond issuance which expedited implementation of the adaptive system on Port St. Lucie Boulevard by approximately 5 years. The project was implemented in fiscal year 21/22.

\$48,507,799.08

10-YEAR GOAL

\$100,000,000.0

LOCATIONS	PERCENTAGE COMPLETE	START DATE	END DATE	ESTIMATED BUDGET	REVISED BUDGET ¹	CONTRACT VALUE
 Southbend to Elkcam Design CEI* Construction 	100% 100% 100%	05/2019 05/2019 ² 09/2020 09/2020	03/2022 12/2020 03/2022 07/2022	\$8,000,000 \$880,000 \$1,200,000 \$5,920,000	\$8,000,000	\$1, 27,598 \$1,381,774
Elkcam to CrosstownDesignCEI*Construction	100% 77% 90%	01/2020 01/2020 001/2022 08/2022	06/2024 01/2022 12/2024 12/2024	\$9,000,000 \$990,000 \$1,350,000 \$6,660,000	\$31,000,000 \$1,300,000 \$2,700,000 \$27,000,000	\$1,484,288 ² \$2,625,991 \$31,579,850 ³
 Crosstown to Prima Vista Design CEI* Construction 		01/2020 01/2020 04/2024 05/2024	06/2026 08/2022 06/2026 04/2026	\$8,000,000 \$880,000 \$1,200,000 \$5,920,000	\$61,000,000 \$1,300,000 \$5,000,000 \$54,700,000	\$1,376,307 ²

^{*}CEI: Construction Engineering Inspection Services

 $^{^3}$ Phase 2 Construction Cost funded by the $\frac{1}{2}$ Cent Sales Tax is \$28,664,870 and \$2,914,980 to be paid from Utilities







¹ Budgets have been revised for certain projects based upon escalating construction costs, which has been offset by higher-than-expected revenue.

² Phase 2 & 3 Amendment #7 = \$74,503 additional pond design, Phase 3 additional design for baffle boxes

\$2,036,752.79

10-YEAR GOAL

\$2,000,000.00

LOCATIONS	PERCENTAGE COMPLETE	START DATE	END DATE	ESTIMATED BUDGET	CONTRACT VALUE
California RoundaboutDesignCEI*Construction	100% 100% 100%	01/2019 1/17/19 10/2019 10/2019	06/2020 06/2019 06/2020 06/2020	\$1,000,000 \$110,000 \$150,000 \$740,000	\$148, 992 \$1,3,05 \$769,769 ¹
Cashmere RoundaboutDesignCEI*Construction	100% 100% 100%	01/2019 1/21/19 10/2019 10/2019	06/2020 06/2019 06/2020 06/2020	\$1,000,000 \$110,000 \$150,000 \$740,000	\$146,579 \$1,7,105 \$786,7201

^{*}CEI: Construction Engineering Inspection Services

¹Original contract funded by the ½ Cent Sales Tax was \$1,392,059 and \$69,736 funded by Utilities. Amendment #1-4 and CO#1 adjusted the ½ Cent Sales Tax contract for Torino/Cashmere to \$749,731 Torino/Cashmere and Torino/California to \$737,022. New construction contract total funded by ½ Cent Sales Tax is \$1,486,753. Values noted in table above include portions funded by Utilities to encapsulate the full contract value.



Torino/Cashmere Roundabout



US 1 IMPROVEMENTS



\$3,529,953.23

10-YEAR GOAL

\$1,500,000.00

TASK	PERCENTAGE COMPLETE	START DATE	END DATE	ESTIMATED BUDGET	REVISED BUDGET	CONTRACT VALUE
Landscaping & Irrigation Within City Limits CEI Construction	97% 97%	08/2022 03/2023	12/2023 12/2023	\$1,500,000 \$300,000 \$1,200,000		\$287,208 \$3,303,956*

^{*}DIFFERENCE OF \$2,487,967 BETWEEN BUDGET AND CONTRACT AMOUNT IS FUNDED BY MOBILITY FEES








FOR MORE INFORMATION, PLEASE VISIT: CITYOFPSL.COM/SALESTAX

SPECIAL NOTES:

- (1) **Only active projects are listed.** The <u>Sidewalk Master Plan</u> is being updated to include the Sales Tax funding. The update will be presented to City Council at the Summer Retreat.
- (2) **Only active projects are listed.** The <u>Repaving Master Plan</u> is being updated to include the Sales Tax funding. The update will be presented to City Council at the Summer Retreat.



CITY OF PSL HALF-CENT SALES TAX MISC. EXPENDITURES

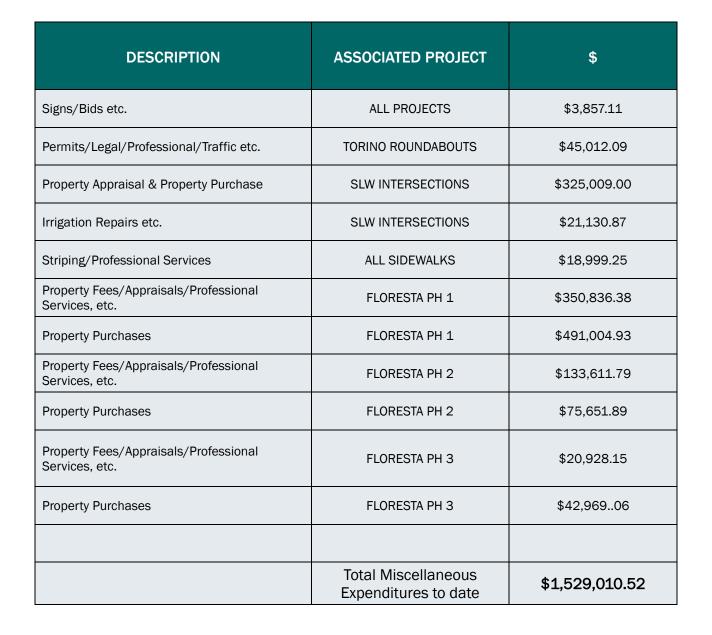



CITY OF PSL HALF-CENT SALES TAX EXPENDITURES

OBJECT	TOTAL 10 YEAR ADVERTISED	REVISED	INVOICES TO DATE FY24/25	PRIOR FISCAL YEARS'	GRAND TOTAL SPENT/INVOICED	BUDGET
EXPENDITURES	BUDGET	BUDGET	ACTUAL	EXPENDITURES	TO DATE	REMAINING
ST LUCIE WEST BOULEVARD	13,200,000	18,300,000	0	1,032,035	1,032,035	17,267,965
SIDEWALKS	11,000,000	11,000,000	0	5,336,391	5,336,391	5,663,609
REPAVING	27,500,000	27,500,000	0	8,198,547	8,198,547	19,301,453
TRAFFIC SIGNAL COORDINATION	1,700,000	-	-	-	-	-
FLORESTA DRIVE	25,000,000	100,000,000	525,254	47,982,545	48,507,799	51,492,201
TORINO INTERSECTION IMPROVEMENTS	2,000,000	2,000,000	-	2,036,753	2,036,753	-36,753
US 1 IMPROVEMENTS	1,500,000	3,700,000	11,675	1,518,278	3,529,953	170,047
MISCELLANEOUS	-	-	9,542	1,519,469	1,529,011	-1,529,011
INTEREST ON INTERNAL BORROWING	1,107,461	0	-	-	-	0
CONTINGENCY/ PARTICIPATORY BUDGETING	6,694,251	3,516,739	-	-	-	3,516,739
TOTAL EXPENDITURES	\$89,701,712	\$166,016,739	\$546,471	\$69,624,018	\$70,170,489	\$95,846,250

^{*}Reduced "Traffic Signal Coordination" Budget by removing \$1,700,000 earmarked for Crosstown Parkway and Port St. Lucie Boulevard Signal upgrades. These projects were expedited and funded by the Crosstown Parkway Extension project and a bond issuance. \$1,700,000 was removed from traffic signal coordination and will be utilized to offset other project cost increases.



^{**}US 1 Improvements \$1,500,000 funded by Half Cent Sales Tax and \$2,487,967 by Mobility Fees.

CITY OF PSL HALF-CENT SALES TAX REVENUE

RECEIPT DATE	MONTH	BUDGETED	ACTUAL CASH
FY 2018-19	Total Cash FY 18 - 19	\$4,375,000	\$4,340,333
FY 2019-20	Total Cash FY 19 - 20	\$7,653,300	\$7,996,372
FY 2020-21	Total Cash FY 20 - 21	\$7,921,469	\$9,537,550
FY 2021-22	Total Cash FY 21 - 22	\$8,388,493	\$12,071,124
FY 2022-23	Total Cash FY 22 - 23	\$10,348,715	\$13,007,024
FY 2023-24	Total Cash FY 23 - 24	\$12,318,575	\$13,531,305
FY 2024-25	Subtotal Cash November 2024	\$2,142,400	\$2,508,481
ALL FISCAL YEARS HCSTx	Total Cash to date	\$53,147,952	\$62,992,190
Other Funding	Mobility Fees Utilities Grants Interlocal Agreement		\$2,487,967 \$3,961,786 \$672,472 \$337,758
ALL FISCAL YEARS	Total Invoices to date		(\$70,170,489)
ALL FISCAL YEARS	Total Cash Available: (Total Cash less Total Invoices)		\$281,684

[•] This is a cash basis report. Therefore, it will not match the accrual basis financial statement revenue numbers.

